ID	Task Name	Duration	Start	Finish
1	**SCARBOROUGH LEISURE VILLAGE**	**1060 days**	**Wed 21/07/10**	**Sat 09/08/14**
2				
3	**Development Briefs**	**130 days**	**Wed 21/07/10**	**Mon 17/01/11**
4	Recruit planners	3 mons	Wed 21/07/10	Mon 11/10/10
5	Prepare briefs	6 wks	Tue 12/10/10	Mon 22/11/10
6	Public consultation	1 mon	Tue 23/11/10	Mon 20/12/10
7	Adoption of briefs	1 mon	Tue 21/12/10	Mon 17/01/11
8				
9	**Prequalification**	**83 days**	**Wed 21/07/10**	**Thu 11/11/10**
10	Draft OJEU Notice, PIM, PQQ	1 mon	Wed 21/07/10	Mon 16/08/10
11	Legal checks	10 days	Tue 17/08/10	Mon 30/08/10
12	Issue OJEU Notice	1 day	Tue 31/08/10	Tue 31/08/10
13	Expression of Interest	22 days	Wed 01/09/10	Thu 30/09/10
14	PQQ assesment	2 wks	Fri 01/10/10	Thu 14/10/10
15	Prepare ICM Report and publish agenda	2 wks	Fri 15/10/10	Thu 28/10/10
16	Call in period	5 days	Fri 29/10/10	Thu 04/11/10
17	Decision implementable	0 days	Thu 04/11/10	Thu 04/11/10
18	Notify bidders	1 wk	Fri 05/11/10	Thu 11/11/10
19				
20	**Dialogue Phase**	**492 days**	**Tue 17/08/10**	**Wed 04/07/12**
21	**ISOP**	**256 days**	**Tue 17/08/10**	**Tue 09/08/11**
22	Prepare ISOP documents	2 mons	Tue 17/08/10	Mon 11/10/10
23	Legal checks	20 days	Tue 12/10/10	Mon 08/11/10
24	Issue ISOP document	1 day	Tue 18/01/11	Tue 18/01/11
25	Dialogue	6 mons	Wed 19/01/11	Tue 05/07/11
26	Evaluation	1 mon	Wed 06/07/11	Tue 02/08/11
27	Notifications	1 wk	Wed 03/08/11	Tue 09/08/11
28	**ISDS**	**201 days**	**Wed 15/06/11**	**Wed 21/03/12**
29	Prepare ISDS documents	3 mons	Wed 15/06/11	Tue 06/09/11
30	Legal checks	20 days	Wed 07/09/11	Tue 04/10/11
31	Issue ISOP document	1 day	Wed 05/10/11	Wed 05/10/11
32	Dialogue	6 mons	Thu 06/10/11	Wed 21/03/12
33	Close dialogue	0 days	Wed 21/03/12	Wed 21/03/12
34	**BAFO**	**75 days**	**Thu 22/03/12**	**Wed 04/07/12**
35	Submission of BAFA	1 mon	Thu 22/03/12	Wed 18/04/12
36	Evaluation of BAFO	1 mon	Thu 19/04/12	Wed 16/05/12
37	Report outcome to Members	1 mon	Thu 17/05/12	Wed 13/06/12
38	Council decision	0 days	Wed 13/06/12	Wed 13/06/12
39	Notifications	1 wk	Thu 14/06/12	Wed 20/06/12
40	Alcatel period	10 days	Thu 21/06/12	Wed 04/07/12
41				
42	**Contracts**	**40 days**	**Thu 05/07/12**	**Wed 29/08/12**
43	Prapare final contracts	20 days	Thu 05/07/12	Wed 01/08/12
44	Execution of contracts	20 days	Thu 02/08/12	Wed 29/08/12
45				
46	**Construction**	**508 days**	**Thu 30/08/12**	**Sat 09/08/14**
47	Mobilisation period	4 wks	Thu 30/08/12	Wed 26/09/12
48	Construct football ground	12 mons	Thu 27/09/12	Tue 27/08/13
49	Operational for Season 2014/15	0 days	Sat 09/08/14	Sat 09/08/14
50	Construct leisure centre (assumed twin t	12 mons	Thu 27/09/12	Tue 27/08/13
51	Fit out leisure centre	1 mon	Wed 28/08/13	Tue 24/09/13
52				
53	**Filey Rd & Seamer Rd Deveopments**	**0 days**	**Tue 24/09/13**	**Tue 24/09/13**
54	Development may commence	0 days	Tue 24/09/13	Tue 24/09/13

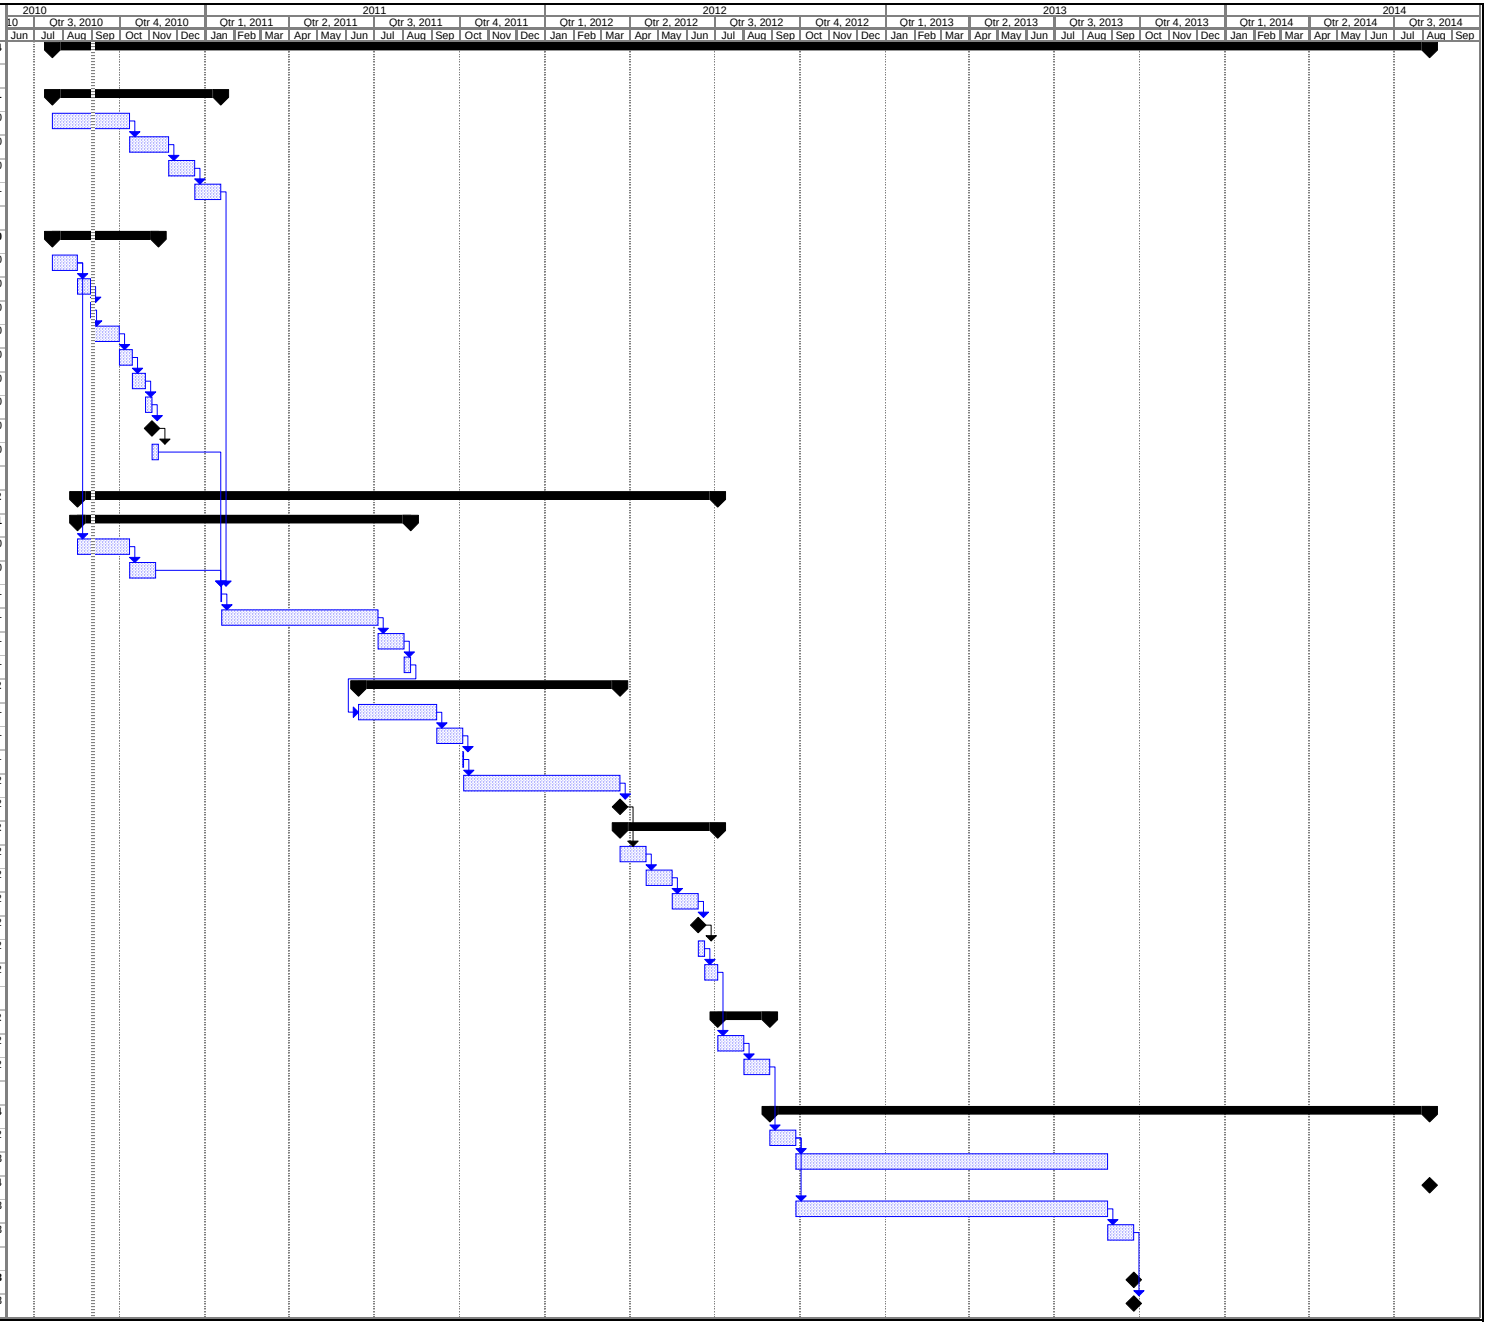

Project: Master Programme
Date: Wed 01/09/10

Task | Progress | Summary | Rolled Up Critical Task | Rolled Up Progress | External Tasks | Group By Summary
Critical Task | Milestone | Rolled Up Task | Rolled Up Milestone | Split | Project Summary | Deadline
